


The High School Project: Minnie Howard Redevelopment

Project Update

Virtual Community Meeting Office of Capital Programs, Planning and Design February 13, 2023







PARA ESPAÑOL, SELECCIONE "Español"



ለአማርኛ "Amharic" የሚለው ይምረጡ



لسماع الترجمة باللغة العربية، اختر "Arabic"











Agenda

- Introduction
- Design Highlights and Renderings
- Project Timeline, Progress and Budget
- High School Educational Redesign Update
- Next Steps and Communications
- Q & A













Introductions

- Azuka Bartlett, Director of Capital Programs, Planning, and Design
- Arte'a Funderburk, CIP Communications Specialist
- Peter Balas, Executive Principal, Alexandria City High School
- Alexander Duncan III, Campus Administrator, Minnie Howard Campus, Alexandria City High School
- **Ken Terzian**, Project Manager, *Perkins Eastman Architects*
- **Eric Fritz**, Superintendent, Gilbane Building Company
- **Gregory Burstein**, Senior Project Manager









Minnie Howard Campus Design











Design - Exterior Renderings















Design - Interior Renderings













Design - Interior Renderings













Design - Interior Renderings













Construction Timeline

Phase 1 - New Minnie Howard Building Construction

Spring 2022:

Construction Mobilization to Site Summer 2022:

Site Clearing Activities Summer 2022- Spring 2023

Foundations and Structure Installation

Spring 2023 - Winter 2023:

Facade and MEP
Infrastructure

Winter 2023-Spring 2024

Interior Finishes Work **Spring 2024:**

Phase 1 Completion Summer 2024 - Early Fall 2024:

Existing
Building
Demolition

Early Fall 2024 - Winter 2025:

Geothermal Well Field Installation Winter 2025 -Early Summer 2025:

Athletic Fields Installation Summer 2025:

Phase 2 Completion

Phase 2 - New Athletic Fields Construction



*Note: These are tentative dates and subject to change









Timelapse













Construction Progress Photos

















Construction Progress Photos

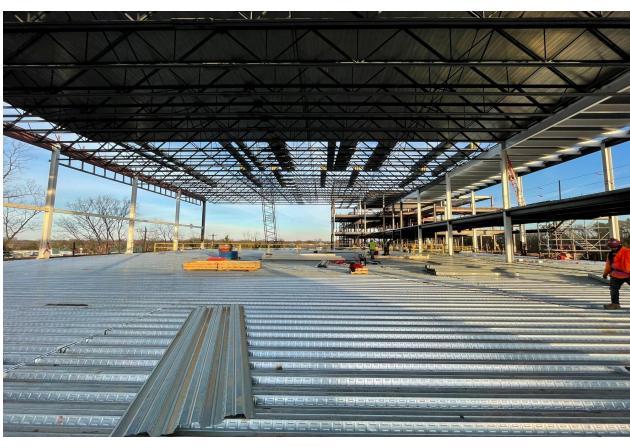

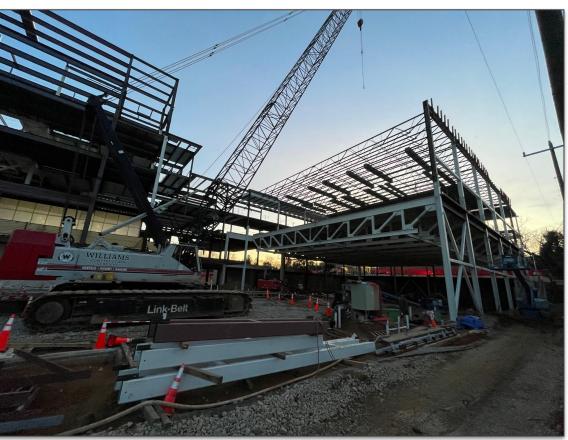












Construction Progress Photos



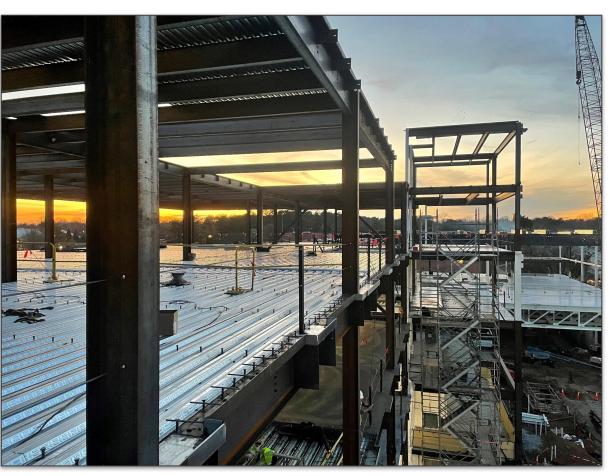











Construction Budget

PHASE	COST
Phase 1: New Building	\$173,789,165
Phase 2: Fields Estimate *To be procured Summer 2023*	\$13,916,545
Total	\$187,705,710











New Educational Spaces

- Increase capacity from 850 to 1600.
- Include students in grades 9-12
- Include 5 floors with an aquatics facility
- Include specific lab spaces for CTE courses
 (e.g. including potential new offerings in game
 design/development, robotics, emergency medical
 sciences, cyber security, firefighting, and more!)













ACHS Educational Programming Goals

Create student pathways and instructional experiences that develop students readiness for college, career, and civic life:

- Opportunities to earn industry credentials
- Work-based learning and workplace readiness skills
- Project-based learning


























Educational Design Next Steps

- Solidifying pathways and programs
- Community and educational partnerships
- Academic advising and course selection will play a role in determining student-based campus
- Operations and logistics including transition between campuses
- HR and Staffing













Next Steps and Communication

- Construction Phase: Ongoing
- Next Community Meeting:
 - Fall/Winter 2023
- Communications:
 - Information communicated on the <u>The High School Project Webpage</u>
 - Sign up for our <u>CIP Newsletter</u>
 - Community members can send questions, comments and concerns to: <u>askACPS@acps.k12.va.us</u> or <u>hsproject@acps.k12.va.us</u>











Contacts

Erika Gulick, Executive Director for Facilities erika.gulick@acps.k12.va.us

Azuka Bartlett, Director of Capital Programs, Planning, and Design <u>azjargal.bartlett@acps.k12.va.us</u>

Arte'a Funderburk, CIP Communications Specialist artea.funderburk@acps.k12.va.us

Dr. Wendy Gonzalez, Chief of Teaching, Learning and Leadership wendy.gonzalez@acps.k12.va.us

Dr. Pierrette Finney, Executive Director of School Leadership pierrette.finney@acps.k12.va.us



Questions?



Interim Superintendent
Dr. Melanie Kay-Wyatt

School Board

Meagan L. Alderton, Chair Jacinta Greene, Vice Chair

Willie F. Bailey, Sr. Kelly Carmichael Booz Abdel-Rahman Elnoubi Christopher Harris Tammy Ignacio Michelle Rief Ashley Simpson Baird
