

**CBS** Corporation

Bloomington Project  
P.O. Box 997  
Bloomington, IN 47402  
(812) 334-0030  
(812) 334-7855 (Fax)

WEEKLY PROJECT STATUS REPORT  
BENNETT'S DUMP SITE

DATE: November 2, 1999

FROM: Brad Brees

TO: Tom Alcamo, USEPA                      Mike Hessling, PSARA  
Vince Epps, IDEM                          Dave Delaney, WRS  
Phil Schonhoff, IDEM                      Alvy Sanders, WRS  
Dottie Alke, CBS                            Dennis Williamson, Monroe County  
Jim Patrick, CBS                            John Langley, CBU  
Ray Taylor, CBS

SUBJECT: Weekly Progress Status Report – October 26 thru November 1, 1999

This report is intended to provide a weekly project update regarding the major developments for the remediation work at Bennett's Dump. Included are progress updates, sample analytical results, schedule updates, waste shipping information and field change decisions. Complete sampling logs, shipping logs and air monitoring and meteorological data logs are available at the site.

**Bennett's Dump Project Site Activities - October 26 – November 1, 1999**

- 73 trucks shipped 1,856.38 tons of material to EQ for disposal during week of 10/26/99. The final 9 trucks were shipped on 10/29/99. A final total of 36,157.62 tons has been shipped for the project.
- No capacitors were recovered during the week of 10/26/99. A final total of 1,756 capacitors has been recovered thru for the project.
- 1 final roll-off with 3.86 tons of capacitors was shipped this week. A total of 9 roll-offs at 121.16 tons was shipped for the project.
- A final 12,700 gallons of water was treated this week. A total of 119,888 gallons was treated for the project
- Completed backfilling areas sampled and confirmed clean.
- Continued deconning and demobing equipment.
- Continued perimeter air sampling. Last day of perimeter air sampling was 10/29/99. Analytical data is attached.

**Bennett's Dump Planned Site Activities – November 2 – November 7, 1999**

- Finish grading and seeding clay cover.
- Finish demobing equipment.
- Site walk through planned for November 3, 1999.

**No More Weekly Meetings for Bennett's Dump!**

Comments or questions regarding this report should be directed to Jim Patrick on 812-334-0030 or Mike Hessling on 812-332-1240 or Ray Taylor on 412-642-2549.

# WEEKLY PROJECT STATUS REPORT

CBS CORPORATION  
BENNETT'S DUMP REMEDIATION SITE

## BENNETT'S DUMP PROJECT

**Reporting Period:** Oct 25, 1999 Through Oct 31, 1999

### Transportation and Disposal Summary:

Trucks Shipped thru Prior Week: 1376 Tons Shipped thru Prior Week: 34,301.24

Date	Truck: Loads	Daily Tons
Monday 10/25/99	21	532.10
Tuesday 10/26/99	18	469.31
Wednesday 10/27/99	25	626.30
Thursday 10/28/99	0	0.00
Friday 10/29/99	9	228.67
Saturday 10/30/99	0	0.00
Sunday 10/31/99	0	0.00

Trucks Shipped this Week: 73 1,856.38 :Tons Shipped this Week

Trucks Shipped to Date: 1449 36,157.62 :Tons Shipped to Date

\* tons estimated using onsite weights

### Capacitor Offsite Disposal/Incinerator Record

Capacitors Recovered this week: 0 Capacitors Recovered to Date: 1756

Roll-offs Shipped: 9 Tons of capacitors Shipped to Date: 121.2

### Air Monitoring Summary:

PUF Samples Collected This Reporting Period:	<u>30</u>	Total to Date:	<u>207</u>
PUF Samples Sent for Lab Analysis This Period:	<u>9</u>	Total to Date:	<u>68</u>
Personnel Samples This Reporting Period:	<u>1</u>	Total to Date:	<u>19</u>

Date	PUF Result (µg/m3)	Downwind Direction	Personnel Results	Compound Analyzed
Monday 10/18/99	15	North		
	ND	Blank		
Tuesday 10/19/99	19.4	West		
Wednesday 10/20/99	14.5	North	await data	VOCs
Thursday 10/21/99	20	South		
	ND	Blank		
Friday 10/22/99	4.3	North		
Saturday 10/23/99	7.2	North		
Sunday 10/24/99	9.3	West		

NA=No Material Handling/No Air Monitoring ND=No Detection

## Water Treatment Summary:


Total Wastewater Treated thru Prior Week: 107,188 gallons

<u>Date</u>		<u>Gallons Treated</u>	<u>PCB Sample Results</u>
Monday	10/25/99	0	_____
Tuesday	10/26/99	12,700	_____
Wednesday	10/27/99	0	_____
Thursday	10/28/99	0	_____
Friday	10/29/99	0	_____
Saturday	10/30/99	0	_____
Sunday	10/31/99	0	_____

Total Treatment for this Week: 12,700

Total Gallons Treated to Date: **119,888**

1 2 3 4 5 6 7 8 9 10 11 12 13 14 15 16 17 18

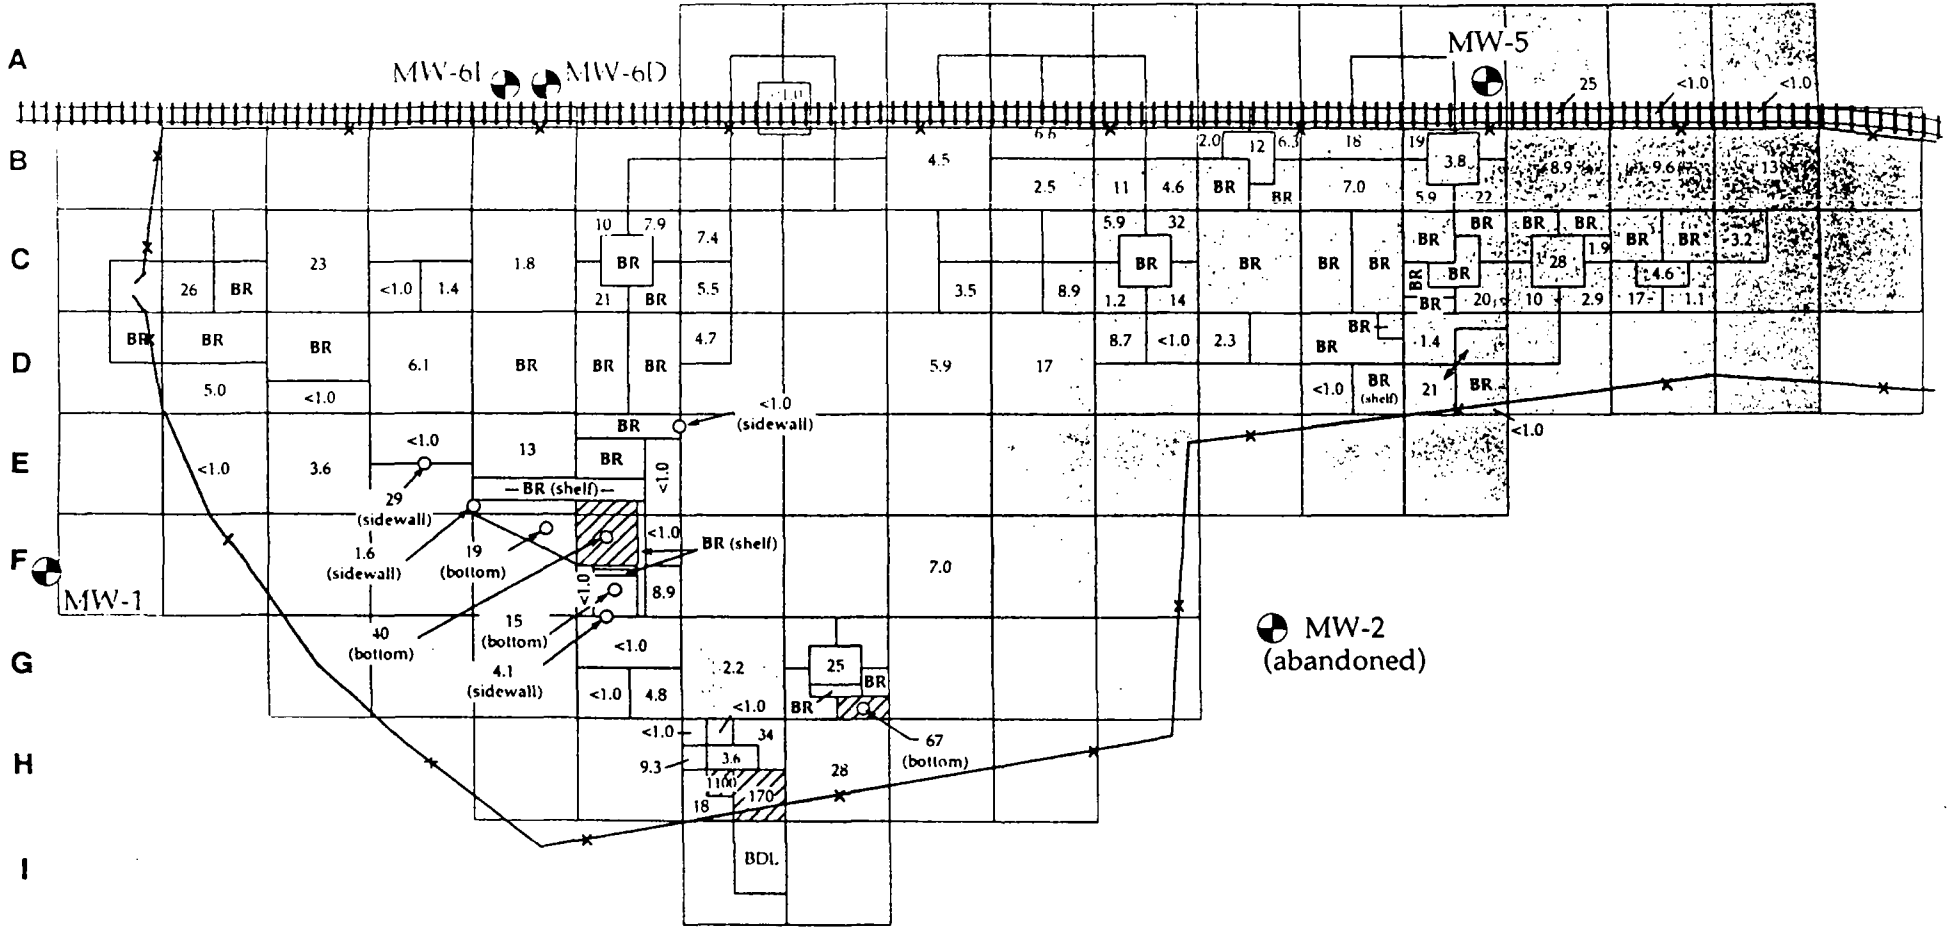



BDL 11/17 Results.dwg



LEGEND	
<input type="checkbox"/>	Delineation grid determined as not PCB-impacted
<input checked="" type="checkbox"/>	Excavation terminated and backfilled
<input type="checkbox"/>	Excavation complete: final PCB result shown, ppm
BR	Verification grid or subgrid excavated to bedrock

No.	Revision	By	Date

<b>CBS CORPORATION</b>		
Excavation Progress Map with PCB Verification Sampling Results as of October 26, 1999 Bennett's Dump, Bloomington, Indiana		
Transmitted By: SAS	Date: 10/26/99	Scale: As Shown

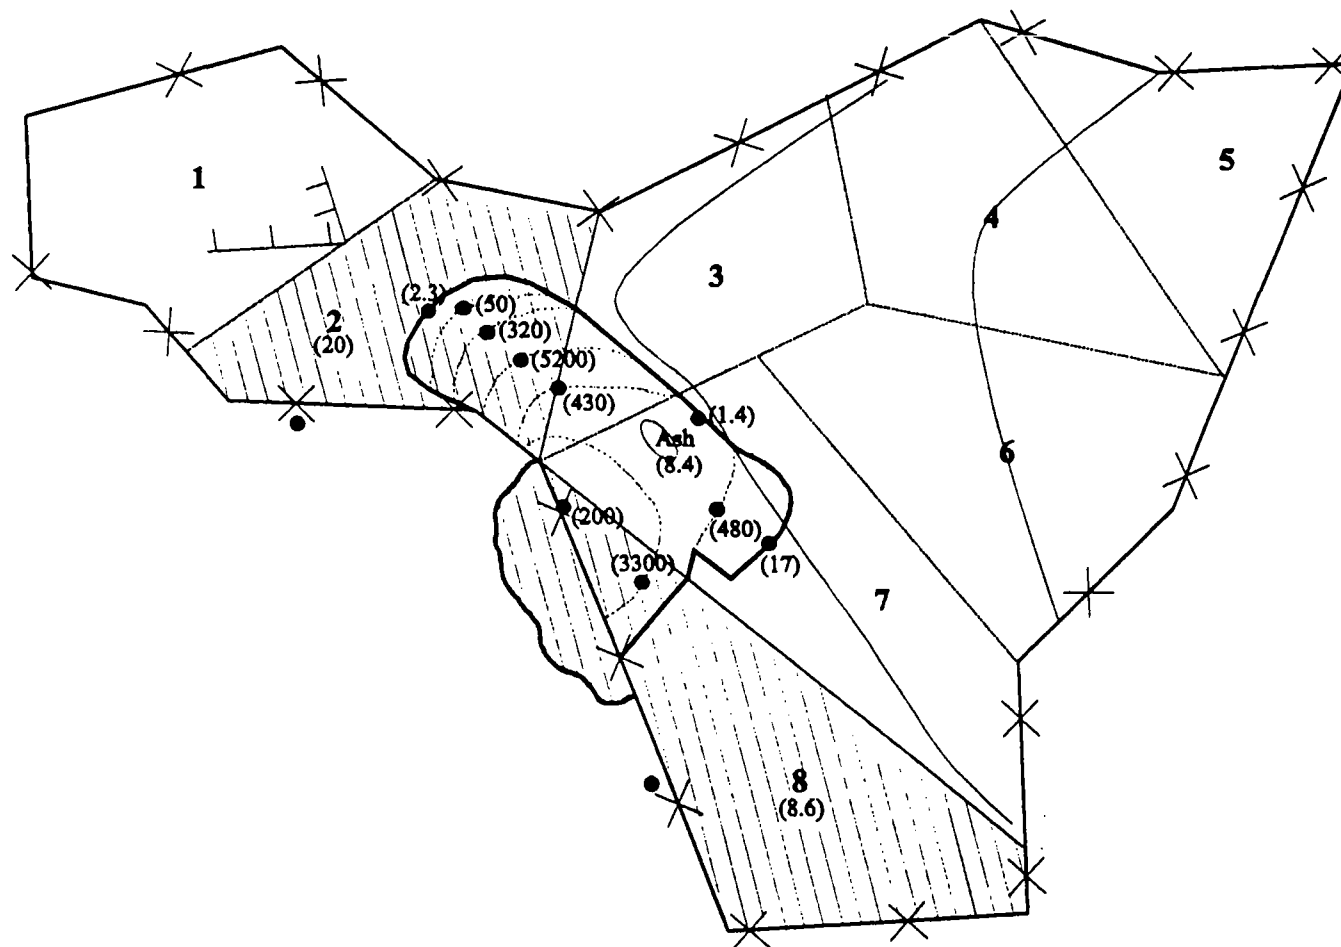

**LEGEND**

- Sidewall Sample w/ PCBs >50 ppm
- ▨ Area determined to contain PCBs >50 ppm
- Grid Demarcation Line (approximate)
- Sidewall sample containing PCBs <50 ppm.
- Area determined as not PCB impacted
- ▨ Area determined to contain PCBs <50 ppm after excavation.

**CBS CORPORATION**

Satellite Area Grid Layout  
and PCB Results  
As of October 22, 1999  
Bennett's Dump, Bloomington, Indiana

Project Number: 30006.77	Scale: 1" = 30'	Checked By: SAS	Drawn By: SAS	Date: 10/22/99
-----------------------------	--------------------	--------------------	------------------	-------------------

