



## JGP Lakedale

# North Whiteley Development

## **BRIEFING NOTE**

North Whiteley Forum 18 February 2021

A095256 17th February 2021

#### **1.** North Whiteley Development Update

#### **1.1 Update on Progress – Reserved Matters Applications**


Current progress is summarised in the table below.

| NORTH    |                  | - RESERV    | ED N  | VATTE  | RS PL/ | ANNIN                | ig appi  | LICATIONS        |  |         | 15   | 5-Jan-20 |
|----------|------------------|-------------|-------|--------|--------|----------------------|----------|------------------|--|---------|------|----------|
| Planning | Developer        | Parcel      | Total | Afford |        |                      |          | Drawing          |  | Net Dev | Аррі | proved   |
| Ref      |                  |             | Nr    |        | Rent   | Sh Own               | Discount | Author           | Number   | Ac      |      |          |
| 18/02170 | Crest            | 22b(Crest)  | 69    | 0      | 0      | 0                    | C        | Powelldobson     | 16023(05) 101 Rev VV                                       | 5.910   | 26/0 | 07/2019  |
| 18/02606 | Bovis            | 1, 2 & 3    | 168   | 51     | 24     | 8                    | 19       | Thrive           | BOVI180635 SL.01_N Rev B                                   | 10.430  | 31/0 | 05/2019  |
| 18/02607 | Bovis            | 26 & 31A    | 160   | 22     | 13     | 4                    | 5        | Thrive           | BOVI180635 SL.01_S Rev G                                   | 9.255   | 12/0 | 04/2019  |
| 19/00419 | Taylor Wimpey    | 22b (TW)    | 91    | 17     | 7      | 4                    | 6        | Cooper Baillie   | CB_83_041_1B_002 Rev F                                     | 5.275   | 28/0 | 05/2019  |
| 19/01142 | Taylor Wimpey    | 29 & 34     | 182   | 25     | 10     | 6                    | 9        | Cooper Baillie   | CB_83_041_P1_102 Rev -                                     | 11.535  | 08/1 | 11/2019  |
| 19/02539 | Crest            | 27          | 59    | 6      |        | 6                    |          | ECE Architecture | 6794/(PL) 002 Rev C  |         | 20/1 | 11/2020  |
| 20/00108 | Taylor Wimpey    | 25A         | 81    | 12     | Brea   | <mark>kdown a</mark> | waited   | Cooper Baillie   | CB_83_041_P2_101 Rev -                                     |         | 27/1 | 11/2020  |
| 20/00572 | Foreman<br>Homes | 24 & 25     | 184   | 37     | 18     | 19                   | C        | HGP Architects   | 19.062.02 Rev H  |         | No   |          |
| 20/00754 | Vistry           | 4,6,7,10,12 | 449   | 0      | 15     | 10                   | 21       | Thrive           | BOVI180635 SL.01_4_7 Rev<br>A<br>BOVI180635 SL.10_12 Rev A |         | 13/1 | 11/2020  |
| 20/02328 | Persimmon        |             | 207   | 30     | 13     | 7                    | 10       | Persimmon Homes  | A-02-015-SL  |         | No   |          |
| Totals   |                  |             | 1650  |        | 100    | 64<br>32.00%         | 70       |                  |  | 42.405  |      |          |

Table 1: Planning Progress

#### **1.2 Update on Current Progress – On Site Highways**

#### <u>Key Plan</u>

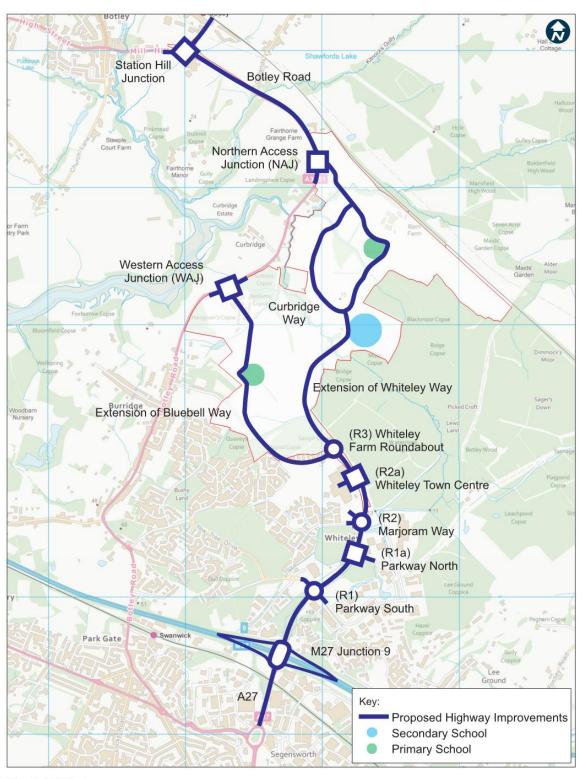

<u>North Whiteley</u> <u>Overview Plan</u> November 2020 North Whiteley Consortium



### **Bluebell Way**

Bluebell Way was opened to through traffic on the 12<sup>th</sup> February 2021.

The road has been opened in a "soft" fashion and its use is being monitored. It should be noted that there is further construction to take place along its length over the course of the next few years.

A series of photographs of the current construction progress are included below:



Plate 1: Western Access Junction @ 21 Jan 2021



Plate 2: Bluebell Way Central – looking north @ 21 Jan 2021

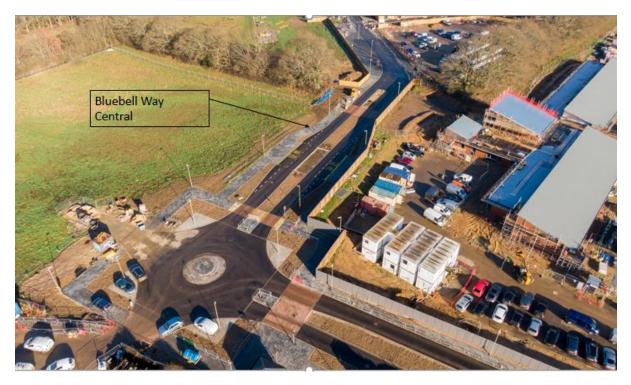


Plate 3: Aerial View West Bluebell Way Central (Squareabout) @ 21 Jan 2021.



Plate 4: Bridge 3 @ 21 Jan 2021.



Plate 5: Bluebell Way Open – view South @ 16 Feb 2021.

### **Cornerstone Primary School**

Hampshire County Council commenced works in May 2020 and continues to make good progress on the new primary school beside Bluebell Way due to open in September 2021.



Plate 6: Cornerstone Primary School @ 21 Jan 2021

### A3051 Botley Road – Northern Access Junction

The main works to complete the junction are complete.



Plate 7: Northern Access Junction & Vistry North @ 21 Jan 2021

### Whiteley Way North / Central & Curbridge Way

Works have commenced and are making good progress. The construction of these roads will form a link between Whiteley Way and Botley Road due to be completed by the end of 2021.



Plate 8: Bridge 1 & Whiteley / Curbridge Way Progress @ 21 Jan 2021



Plate 9: Curbridge Way Progress (view South) @ 21 Jan 2021

### **On Site Whiteley Way (South)**

Works continue on the construction of the first stage of the Whiteley Way extension into the site from Roundabout R3.



Plate 10: Whiteley Way South @ 21 Jan 2021



Plate 11: Whiteley Way South @ 21 Jan 2021

#### **1.3 Update on Current Progress – Housing Parcels**

Three Developers continue work on their parcels. Vistry continue to work on their packages 1, 2 and 3 in the north and 26 & 31A in the south. Crest and Taylor Wimpey continue to work on parcel 22b. Taylor Wimpey continues to work on Packages 29/34. Some 132 new homes now have occupants.

| NORTH    | WHITELEY -    | HOUSI           | NG PROGR              | ESS             |                       |                      |           |          | 31-Jan-21 |
|----------|---------------|-----------------|-----------------------|-----------------|-----------------------|----------------------|-----------|----------|-----------|
|          |               | Parcel          | Total<br>Applications | RMA<br>Approved | Total RMA<br>Approved | Housing Construction |           |          |           |
| Planning | Developer     |                 |                       |                 |                       |                      |           |          | Comments  |
| Ref      |               |                 | Nr                    |                 |                       | Started              | Completed | Occupied |           |
| 18/02170 | Crest         | 22b(Crest       | 69                    | 26/07/2019      | 69                    | 36                   | 17        | 11       |           |
| 18/02606 | Bovis         | 1, 2 & 3        | 168                   | 31/05/2019      | 168                   | 155                  | 75        | 41       |           |
| 18/02607 | Bovis         | 26 & 31A        | 160                   | 12/04/2019      | 160                   | 160                  | 80        | 80       |           |
| 19/00419 | Taylor Wimpey | 22b (TW)        | 91                    | 28/05/2019      | 91                    | 80                   | 19        | 0        |           |
| 19/01142 | Taylor Wimpey | 29 & 34         | 182                   | 08/11/2019      | 182                   | 101                  | 0         | 0        |           |
| 19/02539 | Crest         | 27              | 59                    | 20/11/2020      | 59                    | 0                    | 0         | 0        |           |
| 20/00108 | Taylor Wimpey | 25A             | 81                    | 27/11/2020      | 81                    | 0                    | 0         | 0        |           |
| 20/00572 | Foreman Homes | 24 & 25         | 184                   | No              | 0                     | 0                    | 0         | 0        | -         |
| 20/00754 | Vistry        | 4,6,7,10,1<br>2 | 449                   | 13/11/2020      | 449                   | 10                   | 0         | 0        | -         |
| 20/02328 | Persimmon     | 31, 31b         | 207                   | No              | 0                     | 0                    | 0         | 0        | -         |
| Totals   |               |                 | 1650                  |                 | 1259                  | 542                  | 191       | 132      |           |

Table 2: Housing Construction Progress

# 1.4 Update on Progress – Off Site Highways – Whiteley Way

The s278 Highways design has achieved technical approval (subject to streetlights). The key Environmental and Ecological approvals have also been obtained.

The vegetation clearance between R2 and R3 is now complete. There remain a small number of trees to remove at R2 on the west side.

Advance Service diversion works are ongoing by SSE and SSEET between R1 and R1A but these have been delayed with a current anticipated completion of late April/mid May 2021. Works are being coordinated with the HCC/Skanska works at R1.

A new high voltage cable will be laid in ducts along the eastern side of Whiteley Way between R1A and R3. The linking cable from the Primary Substation is now planned to be laid through the Business area roads rather than down Whiteley Way (R1-R1A).

The opening of the new section of Bluebell Way has created an alternative access point into Whiteley.

#### PHASE 1: Advance Earthworks Embankment between R2 and R3

The contract for these advance off highway embankment works commenced in October and will continue until the end of February 2021. Associated utility ducting works will continue until the end of March.

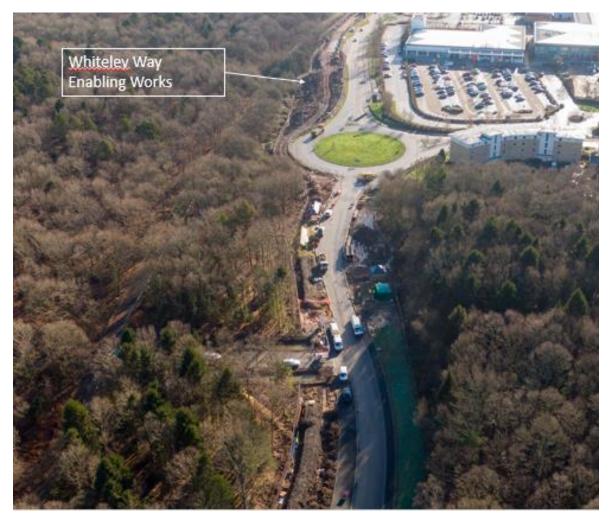


PLATE 12: View of Embankment Works from R3 looking South @ 21 Jan 2021

#### PHASE 2 Highway Works:

Following the completion of the advance works described above it is intended that the main highway improvements will follow. The works have been tendered and proposals for traffic management are being developed.

Timing of Works: May 2021 to June 2022.
