

**TREE ASSESSMENT SCHEDULE**

**Revision No. (Date)**  
Revision A (January 2006)

Job no.: 14898

Project Name: Yuen Long, Kam Tin, Ngau Tam Mei & Tin Shui Wai Drainage Improvement, Stage 1 Phase 2B - Kam Tin

Location : Shek Wu Tong/ Yuen Kong San Tsuen, Kam Tin (KT 14)				Plan Ref. No.: TS-07 to -10				Prepared By : EDAW Ltd.				Date of Report : September 2005				
(a)	(b)	(c)		(d)		(e)	(f)	(g)	(h)	(i)	(j)	(k)	(l)	(m)	(n)	
Tree No.	Dwg. No.	Species		Jurisdiction		Size			Average Health (Good/Fair/Poor)	Form (Good/Fair/Poor)	Survival Rate After Transplanting (High/ Medium /Low)	Amenity Value (High/ Medium /Low)	Recommendation (Retain/ Transplant/ Fell)	Justification for Recommendation	Special Features	Remarks
		Botanical Name	Chinese Name	LCSD	AFCD	Overall Height (metre)	Trunk Diameter (metre)	Crown Spread (metre)								
T122	TS-07	<i>Carica papaya</i>	番木瓜		*	4	0.13	1	Fair	Fair	Low	Low	Retain	Not affected by proposed works	-	vined
T123	TS-07	<i>Tamarindus indica</i>	羅望子		*	4	0.10	4	Good	Good	Low	Medium	Retain	Not affected by proposed works	-	-
T124	TS-07	<i>Dimocarpus longan</i>	龍眼		*	3	0.12	4	Good	Fair	Medium	Medium	Retain	Not affected by proposed works	-	-
T125	TS-07	<i>Ficus superba</i> var. <i>japonica</i>	筆管榕		*	6	0.30	5	Good	Good	High	Medium	Retain	Not affected by proposed works	-	-

Note: The jurisdiction is determined in accordance with Environment, Transport and Works Bureau Technical Circular No.14/2002 for confirmation by relevant departments.

TREE ASSESSMENT SCHEDULE

Revision No. (Date)

Revision A (January 2006)

Revision B (February 2006)

Job no.: 14898

Project Name: Yuen Long, Kam Tin, Ngau Tam Mei & Tin Shui Wai Drainage Improvement, Stage 1 Phase 2B - Kam Tin

Location : Sheu Wu Tong/ Kam Tsin Wai, Kam Tin (KT 15)		Plan Ref. No.: TS-05 to -06							Prepared By : EDAW Ltd.				Date of Report : September 2005			
(a) Tree No.	(b) Dwg. No.	(c) Species		(d) Jurisdiction		(e) Size			(g) Average Health (Good/Fair/Poor)	(h) Form (Good/Fair/Poor)	(i) Survival Rate After Transplanting (High/ Medium /Low)	(j) Amenity Value (High/Medium /Low)	(k) Recommendation (Retain/ Transplant/ Fell)	(l) Justification for Recommendation	(m) Special Features	(n) Remarks
		Botanical Name	Chinese Name	LCSD	AFCD	Overall Height (metre)	Trunk Diameter (metre)	Crown Spread (metre)								
T465	TS-05	<i>Ficus hispida</i>	對葉榕	*	*	4	0.18	4	Fair	Poor	Low	Low	Fell	Affected by proposed works	-	unbalanced form
T466	TS-05	<i>Ficus hispida</i>	對葉榕	*	*	4	0.14	4	Fair	Poor	Low	Low	Fell	Affected by proposed works	-	unbalanced form
T467	TS-05	<i>Cinnamomum camphora</i>	樟	*		6	0.10	1	Poor	Poor	Low	Low	Retain	-	transplant in nursery, outside boundary	unbalanced form, vined
T468	TS-05	<i>Cinnamomum camphora</i>	樟	*		5	0.23	0	Fair	Poor	Low	Low	Retain	-	transplant in nursery, outside boundary	decapitated
T469	TS-05	Dead Tree	死樹	*		-	-	-	-	-	-	-	-	-	-	decapitated
T470	TS-05	<i>Cinnamomum camphora</i>	樟	*		7	0.11	1	Fair	Poor	Low	Low	Transplant	Affected by proposed works	transplant in nursery	-
T471	TS-05	<i>Aleurites moluccana</i>	石栗	*		10	0.33	3	Fair	Fair	High	Low	Transplant	Affected by proposed works	transplant in nursery	-
T472	TS-05	<i>Aleurites moluccana</i>	石栗	*		10	0.32	4	Fair	Fair	High	Low	Transplant	Affected by proposed works	transplant in nursery	-
T473	TS-05	Dead Tree	死樹	*		-	-	-	-	-	-	-	-	-	-	decapitated
T474	TS-05	Dead Tree	死樹	*		-	-	-	-	-	-	-	-	-	-	decapitated
T475	TS-05	<i>Aleurites moluccana</i>	石栗	*		5	0.11	0	Fair	Poor	Low	Low	Transplant	Affected by proposed works	transplant in nursery	-
T476	TS-05	Dead Tree	死樹	*		-	-	-	-	-	-	-	-	-	-	decapitated
T477	TS-05	<i>Aleurites moluccana</i>	石栗	*		7	0.11	2	Fair	Fair	High	Low	Transplant	Affected by proposed works	transplant in nursery	-
T478	TS-05	Dead Tree	死樹	*		-	-	-	-	-	-	-	-	-	-	decapitated
T479	TS-05	<i>Aleurites moluccana</i>	石栗	*		5	0.12	2	Fair	Fair	High	Low	Transplant	Affected by proposed works	transplant in nursery	-
T480	TS-05	<i>Aleurites moluccana</i>	石栗	*		6	0.11	2	Fair	Fair	High	Low	Transplant	Affected by proposed works	transplant in nursery	unbalanced form
T481	TS-05	<i>Aleurites moluccana</i>	石栗	*		10	0.25	4	Fair	Fair	High	Low	Transplant	Affected by proposed works	transplant in nursery	-
T482	TS-05	<i>Aleurites moluccana</i>	石栗	*		7	0.11	2	Fair	Fair	High	Low	Transplant	Affected by proposed works	transplant in nursery	-
T483	TS-05	<i>Aleurites moluccana</i>	石栗	*		4	0.11	2	Fair	Fair	High	Low	Transplant	Affected by proposed works	transplant in nursery	unbalanced form
T484	TS-05	<i>Aleurites moluccana</i>	石栗	*		12	0.25	4	Fair	Fair	High	Low	Transplant	Affected by proposed works	transplant in nursery	-
T485	TS-05	<i>Aleurites moluccana</i>	石栗	*		7	0.12	2	Fair	Fair	High	Low	Transplant	Affected by proposed works	transplant in nursery	-
T486	TS-05	<i>Aleurites moluccana</i>	石栗	*		11	0.27	4	Fair	Fair	High	Low	Transplant	Affected by proposed works	transplant in nursery	-
T487	TS-05	<i>Aleurites moluccana</i>	石栗	*		9	1.40	3	Fair	Fair	High	Low	Transplant	Affected by proposed works	transplant in nursery	-
T488	TS-05	<i>Aleurites moluccana</i>	石栗	*		4	0.10	2	Fair	Fair	High	Low	Transplant	Affected by proposed works	transplant in nursery	-
T489	TS-05	<i>Aleurites moluccana</i>	石栗	*		13	0.30	4	Fair	Fair	High	Low	Transplant	Affected by proposed works	transplant in nursery	-
T490	TS-05	<i>Aleurites moluccana</i>	石栗	*		6	0.11	2	Fair	Fair	High	Low	Transplant	Affected by proposed works	transplant in nursery	-
T491	TS-05	Dead Tree	死樹	*		-	-	-	-	-	-	-	-	-	-	decapitated
T492	TS-05	<i>Aleurites moluccana</i>	石栗	*		2	0.10	1	Poor	Poor	Low	Low	Transplant	Conflict with proposed maintenance access	transplant in nursery	unbalanced form
T493	TS-05	<i>Aleurites moluccana</i>	石栗	*		10	0.27	4	Fair	Fair	High	Low	Transplant	Conflict with proposed maintenance access	transplant in nursery	-
T494	TS-05	Dead Tree	死樹	*		-	-	-	-	-	-	-	-	-	-	decapitated
T495	TS-05	<i>Aleurites moluccana</i>	石栗	*		6	0.10	2	Fair	Fair	High	Low	Transplant	Affected by proposed works	transplant in nursery	-
T496	TS-05	Dead Tree	死樹	*		-	-	-	-	-	-	-	-	-	-	decapitated
T497	TS-05	<i>Aleurites moluccana</i>	石栗	*		14	0.30	4	Fair	Fair	High	Low	Transplant	Affected by proposed works	transplant in nursery	-
T498	TS-05	<i>Aleurites moluccana</i>	石栗	*		14	0.32	6	Fair	Fair	High	Low	Transplant	Affected by proposed works	transplant in nursery	-

**TREE ASSESSMENT SCHEDULE**

**Revision No. (Date)**  
 Revision A (January 2006)  
 Revision B (February 2006)

Job no.: 14898

Project Name: Yuen Long, Kam Tin, Ngau Tam Mei & Tin Shui Wai Drainage Improvement, Stage 1 Phase 2B - Kam Tin

Location : Sheu Wu Tong/ Kam Tsin Wai, Kam Tin (KT 15)				Plan Ref. No.: TS-05 to -06				Prepared By : EDAW Ltd.				Date of Report : September 2005				
(a)	(b)	(c)		(d)		(e)	(f)	(g)	(h)	(i)	(j)	(k)	(l)	(m)	(n)	
Tree No.	Dwg. No.	Species		Jurisdiction		Size			Average Health (Good/Fair/Poor)	Form (Good/Fair/Poor)	Survival Rate After Transplanting (High/ Medium /Low)	Amenity Value (High/ Medium /Low)	Recommendation (Retain/ Transplant/ Fell)	Justification for Recommendation	Special Features	Remarks
		Botanical Name	Chinese Name	LCSD	AFCD	Overall Height (metre)	Trunk Diameter (metre)	Crown Spread (metre)								
T499	TS-05	<i>Aleurites moluccana</i>	石栗	*		6	0.10	2	Fair	Fair	High	Low	Transplant	Affected by proposed works	transplant in nursery	-
T500	TS-05	Dead Tree	死樹	*		-	-	-	-	-	-	-	-	-	-	decapitated
T501-T709	Numbers not used in this feature															
T710	TS-06	<i>Ficus microcarpa</i>	細葉榕	*		5	0.12	4	Fair	Fair	High	Medium	Transplant	Affected by proposed works	-	-
T711	TS-06	<i>Macaranga tanarius</i>	血桐	*		4	0.14	1	Poor	Poor	Low	Low	Retain	Not affected by proposed works	-	-
T712	TS-06	<i>Archontophoenix alexandrae</i>	假檳榔	*		10	0.21	3	Fair	Fair	High	Medium	Transplant	Affected by proposed works	-	-
T713	TS-06	<i>Ficus elastica</i>	印度榕	*		9	0.25	6	Fair	Fair	High	Medium	Transplant	Affected by proposed works	-	-
T714	TS-06	<i>Ficus elastica</i>	印度榕	*		9	0.40	6	Good	Fair	High	Medium	Transplant	Affected by proposed works	-	-
T715	TS-06	<i>Ficus elastica</i>	印度榕	*		4	0.16	4	Fair	Fair	High	Medium	Transplant	Affected by proposed works	-	-
T716	TS-06	<i>Ficus elastica</i>	印度榕	*		5	0.50	6	Fair	Fair	High	Medium	Transplant	Affected by proposed works	-	unbalanced form
T717	TS-06	<i>Archontophoenix alexandrae</i>	假檳榔	*		10	0.21	3	Fair	Fair	High	Medium	Transplant	Affected by proposed works	-	-
T718	TS-06	<i>Ficus microcarpa</i>	細葉榕		*	5	0.50	4	Fair	Fair	High	Medium	Retain	-	outside boundary	unbalanced form
T719	TS-06	<i>Ficus microcarpa</i>	細葉榕		*	10	0.40	5	Fair	Fair	High	Medium	Retain	-	outside boundary	-
T720	TS-06	<i>Ficus microcarpa</i>	細葉榕		*	10	0.35	6	Fair	Fair	High	Medium	Retain	-	outside boundary	unbalanced form
T721	TS-06	<i>Ficus microcarpa</i>	細葉榕		*	8	0.26	5	Fair	Fair	High	Medium	Retain	-	outside boundary	-
T722	TS-06	<i>Ficus microcarpa</i>	細葉榕		*	5	0.10	2	Fair	Fair	High	Medium	Transplant	Affected by proposed works	-	vined
T723	TS-06	<i>Ficus microcarpa</i>	細葉榕	*		2	0.17	3	Fair	Fair	High	Medium	Transplant	Affected by proposed works	-	vined
T724	TS-06	<i>Dimocarpus longan</i>	龍眼		*	3	0.10	3	Poor	Poor	Low	Low	Fell	Affected by proposed works	-	unbalanced form, root exposed, felled down
T725	TS-06	<i>Psidium guajava</i>	番石榴		*	3	0.20	3	Fair	Fair	Medium	Low	Retain	-	outside boundary	unbalanced form
T726	TS-06	<i>Macaranga tanarius</i>	血桐		*	3	0.12	4	Poor	Poor	Low	Low	Retain	-	outside boundary	vined, no leave
T727	TS-06	<i>Macaranga tanarius</i>	血桐		*	3	0.15	2	Fair	Fair	Medium	Low	Retain	Not affected by proposed works	-	unbalanced form
T728	TS-06	<i>Macaranga tanarius</i>	血桐		*	4	0.12	5	Fair	Fair	Medium	Low	Fell	Affected by proposed works	-	multi-trunked
T729	TS-06	<i>Celtis sinensis</i>	朴		*	9	0.32	5	Fair	Fair	Low	Medium	Retain	-	outside boundary	-
T730	TS-06	<i>Macaranga tanarius</i>	血桐		*	2	0.23	2	Poor	Poor	Low	Low	Retain	-	outside boundary	leaning, decapitated
T731	TS-06	<i>Dimocarpus longan</i>	龍眼		*	9	0.21	6	Fair	Fair	Medium	Low	Retain	-	outside boundary	forked
T732	TS-06	<i>Celtis sinensis</i>	朴		*	6	0.15	3	Fair	Poor	Low	Low	Retain	-	outside boundary	unbalanced form, no leave
T733	TS-06	<i>Clausena lansium</i>	黃皮		*	5	0.12	4	Fair	Fair	Medium	Low	Retain	Not affected by proposed works	-	-
T734	TS-06	<i>Carica papaya</i>	番木瓜		*	3	0.18	3	Fair	Fair	Low	Low	Fell	Affected by proposed works	-	-
T735	TS-06	<i>Eriobotrya japonica</i>	枇杷		*	4	0.12	3	Fair	Fair	Low	Low	Fell	Affected by proposed works	-	shrubby
T736	TS-06	<i>Dimocarpus longan</i>	龍眼		*	6	0.10	3	Fair	Fair	Medium	Medium	Transplant	Affected by proposed works	-	-
T737	TS-06	<i>Psidium guajava</i>	番石榴		*	7	0.16	4	Fair	Fair	Medium	Low	Fell	Affected by proposed works	-	shrubby
T738	TS-06	<i>Psidium guajava</i>	番石榴		*	3	0.14	4	Fair	Fair	Medium	Low	Retain	To preserve with tree ring	-	unbalanced form
T739	TS-06	<i>Psidium guajava</i>	番石榴		*	3	0.13	4	Fair	Fair	Medium	Low	Retain	Not affected by proposed works	-	forked

**TREE ASSESSMENT SCHEDULE**

**Revision No. (Date)**

Revision A (January 2006)

Revision B (February 2006)

Job no.: 14898

Project Name: Yuen Long, Kam Tin, Ngau Tam Mei & Tin Shui Wai Drainage Improvement, Stage 1 Phase 2B - Kam Tin

Location : Sheu Wu Tong/ Kam Tsin Wai, Kam Tin (KT 15)				Plan Ref. No.: TS-05 to -06				Prepared By : EDAW Ltd.				Date of Report : September 2005				
(a)	(b)	(c)		(d)		(e)	(f)	(g)	(h)	(i)	(j)	(k)	(l)	(m)	(n)	
Tree No.	Dwg. No.	Species		Jurisdiction		Size			Average Health (Good/Fair/Poor)	Form (Good/Fair/Poor)	Survival Rate After Transplanting (High/ Medium /Low)	Amenity Value (High/ Medium /Low)	Recommendation (Retain/ Transplant/ Fell)	Justification for Recommendation	Special Features	Remarks
		Botanical Name	Chinese Name	LCSD	AFCD	Overall Height (metre)	Trunk Diameter (metre)	Crown Spread (metre)								
T740	TS-06	<i>Psidium guajava</i>	番石榴		*	3	0.12	3	Fair	Fair	Medium	Low	Retain	-	outside boundary	unbalanced form, forked
T741	TS-06	<i>Psidium guajava</i>	番石榴		*	5	0.22	6	Fair	Fair	Medium	Low	Retain	-	outside boundary	-
T742	Number not used in this feature															
T743	TS-05	<i>Cinnamomum camphora</i>	樟	*		6	0.13	2	Poor	Poor	Low	Low	Retain	-	transplant in nursery, outside boundary	unbalanced form, leaning, vined
T744	TS-05	<i>Leucaena leucocephala</i>	銀合歡	*		8	0.18	6	Fair	Fair	Low	Low	Retain	Not affected by proposed works	on slope	-
T745	TS-06	Dead Tree	死樹		*	9	0.54	0	-	-	-	-	Retain	-	outside boundary	-
T746	TS-06	<i>Dimocarpus longan</i>	龍眼		*	5	0.13	5	Fair	Poor	Low	Low	Retain	-	outside boundary	multi-trunked
T747	TS-06	<i>Ficus hispida</i>	對葉榕		*	5	0.22	4	Poor	Poor	Low	Low	Retain	-	outside boundary, at top of wall	unbalanced form, few leave
T748-T800	Numbers not used in this feature															
T801	TS-05	<i>Aleurites moluccana</i>	石栗	*		10	0.25	4	Fair	Fair	High	Medium	Transplant	Conflict with proposed maintenance access	-	-
T802	TS-05	<i>Acacia confusa</i>	台灣相思	*		5	0.20	5	Fair	Poor	Low	Low	Fell	Conflict with proposed maintenance access	-	unbalanced form, vined
T803	TS-05	<i>Melia azedarach</i>	楝	*		4	0.15	2	Poor	Poor	Low	Low	Fell	Conflict with proposed maintenance access	-	unbalanced form, vined
T804	TS-05	<i>Macaranga tanarius</i>	血桐	*		6	0.18	0	Fair	Poor	Low	Low	Fell	Conflict with proposed maintenance access	-	root exposed, unbalanced form
T805	TS-05	<i>Bombax ceiba</i>	木棉	*		7	0.23	3	Fair	Fair	High	Medium	Transplant	Conflict with proposed maintenance access	-	-
T806	TS-05	Dead Tree	死樹	*		-	-	-	-	-	-	-	-	-	-	decapitated
T807	TS-05	<i>Cassia siamea</i>	鐵刀木	*		4	0.20	2	Fair	Poor	Low	Low	Fell	Affected by proposed works	transplant in nursery	unbalanced form
T808	TS-05	<i>Cinnamomum camphora</i>	樟	*		5	0.11	3	Fair	Poor	Low	Low	Transplant	Affected by proposed works	transplant in nursery	decapitated
T809	TS-05	<i>Cassia siamea</i>	鐵刀木	*		3	0.10	0	Poor	Poor	Low	Low	Fell	Affected by proposed works	transplant in nursery	decapitated, multi-trunked
T810	TS-05	<i>Ficus hispida</i>	對葉榕		*	3	0.11	3	Fair	Poor	Low	Low	Retain	Not affected by proposed works	-	unbalanced form, forked
T811	TS-05	<i>Ficus hispida</i>	對葉榕		*	4	0.12	3	Poor	Poor	Low	Low	Retain	Not affected by proposed works	-	few leave, forked, unbalanced form
T812	TS-05	Unidentified	-		*	4	0.25	0	Poor	Poor	Low	Low	Retain	Not affected by proposed works	-	forked, decapitated, root exposed, no leave
T813	TS-05	<i>Bauhinia</i> sp.	羊蹄甲屬		*	2	0.15	1	Fair	Poor	Low	Low	Retain	Not affected by proposed works	-	unbalanced form
T814	TS-05	<i>Cassia siamea</i>	鐵刀木		*	7	0.43	5	Fair	Fair	High	Low	Retain	Not affected by proposed works	-	unbalanced form
T815	TS-05	<i>Cinnamomum camphora</i>	樟		*	3	0.24	0	Fair	Poor	Low	Low	Fell	Affected by proposed works	transplant in nursery	decapitated
T816	TS-05	Dead Tree	死樹	*		-	-	-	-	-	-	-	-	-	-	decapitated
T817	TS-05	Dead Tree	死樹	*		-	-	-	-	-	-	-	-	-	-	decapitated
T818	TS-05	<i>Cinnamomum camphora</i>	樟	*		3	0.23	0	Fair	Poor	Low	Low	Transplant	Affected by proposed works	transplant in nursery	-
T819	TS-05	<i>Cinnamomum camphora</i>	樟	*		4	0.27	0	Fair	Poor	Low	Low	Transplant	Conflict with proposed maintenance access	transplant in nursery	-
T820	TS-05	<i>Cinnamomum camphora</i>	樟	*		10	0.35	4	Fair	Fair	Low	Low	Transplant	Conflict with proposed maintenance access	transplant in nursery	-
T821	TS-05	<i>Cinnamomum camphora</i>	樟	*		6	0.17	3	Fair	Poor	Low	Low	Transplant	Conflict with proposed maintenance access	transplant in nursery	unbalanced form
T822	TS-05	Dead Tree	死樹	*		-	-	-	-	-	-	-	-	-	-	decapitated
T823	TS-05	Dead Tree	死樹	*		-	-	-	-	-	-	-	-	-	-	decapitated

**TREE ASSESSMENT SCHEDULE**

**Revision No. (Date)**

Revision A (January 2006)

Revision B (February 2006)

Job no.: 14898

Project Name: Yuen Long, Kam Tin, Ngau Tam Mei & Tin Shui Wai Drainage Improvement, Stage 1 Phase 2B - Kam Tin

Location : Sheu Wu Tong/ Kam Tsin Wai, Kam Tin (KT 15) Plan Ref. No.: TS-05 to -06 Prepared By : EDAW Ltd. Date of Report : September 2005

(a)	(b)	(c)		(d)		(d)	(e)	(f)	(g)	(h)	(i)	(j)	(k)	(l)	(m)	(n)
Tree No.	Dwg. No.	Species		Jurisdiction		Size			Average Health (Good/Fair/Poor)	Form (Good/Fair/Poor)	Survival Rate After Transplanting (High/ Medium /Low)	Amenity Value (High/ Medium /Low)	Recommendation (Retain/ Transplant/ Fell)	Justification for Recommendation	Special Features	Remarks
		Botanical Name	Chinese Name	LCSD	AFCD	Overall Height (metre)	Trunk Diameter (metre)	Crown Spread (metre)								
T824	TS-05	<i>Cinnamomum camphora</i>	樟	*		4	0.13	2	Poor	Poor	Low	Low	Transplant	Conflict with proposed maintenance access	transplant in nursery	unbalanced form, vined
T825	TS-05	<i>Cinnamomum camphora</i>	樟		*	4	0.32	0	Fair	Poor	Low	Low	Fell	Affected by proposed works	transplant in nursery	decapitated
T826	TS-05	<i>Cinnamomum camphora</i>	樟	*		6	0.10	1	Fair	Poor	Low	Low	Transplant	Affected by proposed works	transplant in nursery	-
T827	TS-05	Dead Tree	死樹	*		-	-	-	-	-	-	-	-	-	-	decapitated
T828	TS-05	Dead Tree	死樹	*		-	-	-	-	-	-	-	-	-	-	decapitated
T829	TS-05	Dead Tree	死樹	*		-	-	-	-	-	-	-	-	-	-	decapitated
T830	TS-05	Dead Tree	死樹	*		-	-	-	-	-	-	-	-	-	-	decapitated
T831	TS-05	<i>Cinnamomum camphora</i>	樟	*		4	0.24	0	Fair	Poor	Low	Low	Transplant	Affected by proposed works	transplant in nursery	-
T832	TS-05	Dead Tree	死樹	*		-	-	-	-	-	-	-	-	-	-	decapitated
T833	TS-05	Dead Tree	死樹	*		-	-	-	-	-	-	-	-	-	-	decapitated
T834	TS-05	Dead Tree	死樹	*		-	-	-	-	-	-	-	-	-	-	decapitated
T835	TS-05	<i>Cinnamomum camphora</i>	樟	*		10	0.32	4	Fair	Fair	Low	Low	Transplant	Affected by proposed works	transplant in nursery	-
T836	TS-05	Dead Tree	死樹	*		-	-	-	-	-	-	-	-	-	-	decapitated
T837	TS-05	Dead Tree	死樹	*		-	-	-	-	-	-	-	-	-	-	decapitated
T838	TS-05	Dead Tree	死樹	*		-	-	-	-	-	-	-	-	-	-	decapitated
T839	TS-05	<i>Cinnamomum camphora</i>	樟		*	5	0.11	1	Fair	Poor	Low	Low	Fell	Affected by proposed works	transplant in nursery	-
T840	TS-05	<i>Cinnamomum camphora</i>	樟		*	4	0.10	0	Fair	Poor	Low	Low	Fell	Affected by proposed works	transplant in nursery	decapitated
T841	TS-05	<i>Celtis sinensis</i>	朴		*	7	0.20	2	Fair	Poor	Low	Low	Fell	Affected by proposed works	transplant in nursery	unbalanced form
T842	TS-05	<i>Celtis sinensis</i>	朴		*	6	0.52	4	Fair	Fair	Low	Low	Fell	Affected by proposed works	transplant in nursery	-
T843	TS-05	<i>Cinnamomum camphora</i>	樟		*	4	0.11	1	Fair	Poor	Low	Low	Fell	Affected by proposed works	transplant in nursery	-
T844	TS-05	<i>Cinnamomum camphora</i>	樟		*	5	0.13	1	Fair	Poor	Low	Low	Fell	Affected by proposed works	transplant in nursery	-
T845	TS-05	<i>Cassia siamea</i>	鐵刀木		*	10	0.32	3	Fair	Fair	High	Low	Transplant	Conflict with proposed maintenance access	transplant in nursery	-
T846	TS-05	<i>Cassia siamea</i>	鐵刀木		*	10	0.34	4	Fair	Fair	High	Medium	Transplant	Affected by proposed works	-	-
T847	TS-05	<i>Cassia siamea</i>	鐵刀木		*	8	0.23	3	Fair	Poor	Low	Low	Fell	Affected by proposed works	twisted with T848	unbalanced form
T848	TS-05	<i>Cassia siamea</i>	鐵刀木		*		0.25	4	Fair	Poor	Low	Low	Fell	Affected by proposed works	twisted with T847	unbalanced form
T849	TS-05	<i>Carica papaya</i>	番木瓜		*	4	0.10	1	Fair	Fair	Low	Low	Retain	-	outside boundary	-
T850	TS-05	<i>Bischofia javanica</i>	秋楓		*	8	0.27	4	Fair	Fair	Medium	Medium	Transplant	Affected by proposed works	-	-
T851	TS-05	<i>Archontophoenix alexandrae</i>	假檳榔		*	4	0.11	3	Fair	Fair	High	Low	Retain	Not affected by proposed works	transplant in nursery	-
T852	TS-05	<i>Macaranga tanarius</i>	血桐		*	1	0.10	0	Poor	Poor	Low	Low	Fell	Affected by proposed works	-	decapitated
T853	TS-05	<i>Morus alba</i>	桑		*	4	0.10	4	Fair	Fair	Low	Medium	Transplant	Affected by proposed works	-	vined
T854	TS-05	<i>Ficus hispida</i>	對葉榕		*	5	0.20	6	Fair	Fair	High	Low	Fell	Affected by proposed works	-	multi-trunked
T855	TS-05	<i>Macaranga tanarius</i>	血桐		*	5	0.21	6	Fair	Poor	Low	Low	Retain	-	outside boundary	multi-trunked
T856	TS-05	<i>Dimocarpus longan</i>	龍眼		*	8	0.33	4	Fair	Fair	Medium	Medium	Transplant	Affected by proposed works	-	-
T857	TS-05	<i>Macaranga tanarius</i>	血桐		*	4	0.20	4	Fair	Fair	Medium	Low	Retain	Not affected by proposed works	-	-

**TREE ASSESSMENT SCHEDULE**

**Revision No. (Date)**  
 Revision A (January 2006)  
 Revision B (February 2006)

Job no.: 14898

Project Name: Yuen Long, Kam Tin, Ngau Tam Mei & Tin Shui Wai Drainage Improvement, Stage 1 Phase 2B - Kam Tin

Location : Sheu Wu Tong/ Kam Tsin Wai, Kam Tin (KT 15) Plan Ref. No.: TS-05 to -06 Prepared By : EDAW Ltd. Date of Report : September 2005

(a)	(b)	(c)		(d)		(e)	(f)	(g)	(h)	(i)	(j)	(k)	(l)	(m)	(n)	
Tree No.	Dwg. No.	Species		Jurisdiction		Size			Average Health (Good/Fair/Poor)	Form (Good/Fair/Poor)	Survival Rate After Transplanting (High/ Medium /Low)	Amenity Value (High/Medium /Low)	Recommendation (Retain/ Transplant/ Fell)	Justification for Recommendation	Special Features	Remarks
		Botanical Name	Chinese Name	LCSD	AFCD	Overall Height (metre)	Trunk Diameter (metre)	Crown Spread (metre)								
T858	TS-05	<i>Litsea glutinosa</i>	潺稿樹		*	4	0.23	3	Fair	Fair	Low	Low	Retain	-	outside boundary	unbalanced form
T859	TS-05	<i>Artocarpus macrocarpus</i>	波羅蜜		*	5	0.10	3	Fair	Fair	Medium	Low	Transplant	Affected by proposed works	-	-
T860	TS-05	<i>Artocarpus macrocarpus</i>	波羅蜜		*	5	0.11	2	Fair	Fair	Medium	Low	Transplant	Affected by proposed works	-	-
T861	TS-05	<i>Artocarpus macrocarpus</i>	波羅蜜		*	5	0.11	2	Fair	Fair	Medium	Low	Transplant	Affected by proposed works	-	-
T862	TS-05	<i>Artocarpus macrocarpus</i>	波羅蜜		*	5	0.10	2	Fair	Fair	Medium	Low	Transplant	Affected by proposed works	-	-
T863	TS-05	<i>Artocarpus macrocarpus</i>	波羅蜜		*	5	0.10	2	Fair	Fair	Medium	Low	Transplant	Affected by proposed works	-	-
T864	TS-05	<i>Artocarpus macrocarpus</i>	波羅蜜		*	5	0.12	2	Fair	Fair	Medium	Low	Transplant	Affected by proposed works	-	-
T865	TS-05	<i>Artocarpus macrocarpus</i>	波羅蜜		*	5	0.11	2	Fair	Fair	Medium	Low	Transplant	Affected by proposed works	-	-
T866	TS-05	<i>Artocarpus macrocarpus</i>	波羅蜜		*	4	0.10	2	Fair	Fair	Medium	Low	Transplant	Affected by proposed works	-	-
T867	TS-05	<i>Dimocarpus longan</i>	龍眼		*	6	0.27	5	Fair	Fair	Medium	Medium	Transplant	Affected by proposed works	-	-
T868	TS-05	<i>Artocarpus macrocarpus</i>	波羅蜜		*	5	0.10	2	Fair	Fair	Medium	Low	Retain	Not affected by proposed works	-	-
T869	TS-05	<i>Artocarpus macrocarpus</i>	波羅蜜		*	5	0.13	2	Fair	Fair	Medium	Low	Retain	Not affected by proposed works	-	-
T870	TS-05	<i>Ligustrum sinense</i>	山指甲		*	5	0.12	4	Fair	Fair	Low	Medium	Transplant	Affected by proposed works	-	-
T871	TS-05	<i>Ficus hispida</i>	對葉榕		*	4	0.13	4	Fair	Fair	High	Low	Retain	-	outside boundary	unbalanced form
T872	TS-05	<i>Ficus hispida</i>	對葉榕		*	4	0.13	4	Fair	Fair	High	Low	Retain	-	outside boundary	unbalanced form
T873	TS-05	<i>Ficus hispida</i>	對葉榕		*	4	0.14	4	Fair	Fair	High	Low	Retain	-	outside boundary	unbalanced form
T874	TS-05	<i>Ficus hispida</i>	對葉榕		*	4	0.14	4	Poor	Poor	Low	Low	Retain	-	outside boundary	unbalanced form
T875	TS-05	<i>Macaranga tanarius</i>	血桐		*	4	0.12	4	Fair	Fair	Medium	Low	Retain	Not affected by proposed works	-	unbalanced form
T876	TS-05	<i>Dimocarpus longan</i>	龍眼		*	7	0.52	6	Good	Fair	Medium	Low	Retain	Not affected by proposed works	-	-
T877	TS-05	<i>Ficus microcarpa</i>	細葉榕		*	5	0.11	4	Fair	Fair	High	Low	Retain	-	outside boundary	vined
T878	TS-05	<i>Dimocarpus longan</i>	龍眼		*	7	0.32	6	Fair	Fair	Medium	Medium	Retain	To preserve with tree well	-	-
T879	TS-05	<i>Macaranga tanarius</i>	血桐		*	5	0.13	5	Fair	Fair	Medium	Low	Fell	Affected by proposed works	-	multi-trunked
T880	TS-05	<i>Melia azedarach</i>	楝		*	7	0.42	4	Fair	Fair	Medium	Medium	Transplant	Affected by proposed works	-	-
T881	TS-05	<i>Dimocarpus longan</i>	龍眼		*	12	0.55	5	Good	Good	Low	High	Retain	To preserve with tree ring	-	mature
T882	TS-05	<i>Dimocarpus longan</i>	龍眼		*	12	0.72	8	Good	Good	Low	High	Retain	-	outside boundary	mature
T883	TS-05	<i>Celtis sinensis</i>	朴		*	8	0.45	5	Fair	Fair	Low	Medium	Transplant	Affected by proposed works	-	-
T884	TS-05	<i>Averrhoa carambola</i>	楊桃		*	4	0.24	4	Fair	Fair	Medium	Medium	Retain	-	outside boundary	-
T885	TS-05	<i>Clausena lansium</i>	黃皮		*	5	0.18	4	Fair	Fair	Medium	Low	Retain	-	outside boundary	-
T886	TS-05	<i>Clausena lansium</i>	黃皮		*	5	0.29	4	Fair	Fair	Medium	Low	Retain	-	outside boundary	-
T887	TS-05	<i>Artocarpus macrocarpus</i>	波羅蜜		*	4	0.10	3	Fair	Fair	Medium	Low	Retain	-	outside boundary	-
T888	TS-05	<i>Dimocarpus longan</i>	龍眼		*	10	0.35	6	Fair	Fair	Medium	Medium	Retain	Not affected by proposed works	-	-
T889	TS-05	<i>Macaranga tanarius</i>	血桐		*	4	0.21	7	Fair	Fair	Medium	Low	Retain	Not affected by proposed works	-	unbalanced form
T890	TS-05	<i>Ficus microcarpa</i>	細葉榕		*	5	0.16	4	Fair	Fair	High	Medium	Transplant	Affected by proposed works	-	-
T891	TS-05	<i>Ficus microcarpa</i>	細葉榕		*	5	0.13	4	Fair	Fair	High	Medium	Transplant	Conflict with proposed maintenance access	-	-

**TREE ASSESSMENT SCHEDULE**

**Revision No. (Date)**

Revision A (January 2006)

Revision B (February 2006)

**Job no.: 14898**

**Project Name: Yuen Long, Kam Tin, Ngau Tam Mei & Tin Shui Wai Drainage Improvement, Stage 1 Phase 2B - Kam Tin**

**Location : Sheu Wu Tong/ Kam Tsin Wai, Kam Tin (KT 15)**

**Plan Ref. No.: TS-05 to -06**

**Prepared By : EDAW Ltd.**

**Date of Report : September 2005**

(a)	(b)	(c)		(d)		(e)	(f)	(g)	(h)	(i)	(j)	(k)	(l)	(m)	(n)	
Tree No.	Dwg. No.	Species		Jurisdiction		Size			Average Health (Good/Fair/Poor)	Form (Good/Fair/Poor)	Survival Rate After Transplanting (High/ Medium /Low)	Amenity Value (High/ Medium /Low)	Recommendation (Retain/ Transplant/ Fell)	Justification for Recommendation	Special Features	Remarks
		Botanical Name	Chinese Name	LCSD	AFCD	Overall Height (metre)	Trunk Diameter (metre)	Crown Spread (metre)								
T892	TS-05	<i>Ficus microcarpa</i>	細葉榕		*	6	0.15	4	Fair	Fair	High	Low	Retain	Not affected by proposed works	-	-
T893	TS-05	<i>Ficus microcarpa</i>	細葉榕		*	6	0.13	4	Fair	Fair	High	Low	Retain	Not affected by proposed works	-	-
T894	TS-05	<i>Ficus microcarpa</i>	細葉榕		*	6	0.16	4	Fair	Fair	High	Low	Retain	-	outside boundary	-
T895	TS-05	<i>Macaranga tanarius</i>	血桐		*	3	0.10	4	Fair	Fair	Medium	Low	Retain	Not affected by proposed works	-	-
T896	TS-05	<i>Ficus microcarpa</i>	細葉榕		*	6	0.13	4	Fair	Fair	Low	Low	Fell	Affected by proposed works	Wall Tree	-
T897	TS-05	<i>Macaranga tanarius</i>	血桐		*	5	0.10	2	Fair	Fair	Medium	Low	Fell	Affected by proposed works	-	forked, unbalanced form
T898	TS-05	<i>Macaranga tanarius</i>	血桐		*	6	0.11	5	Fair	Fair	Medium	Low	Fell	Affected by proposed works	-	forked, unbalanced form
T899	TS-05	<i>Macaranga tanarius</i>	血桐		*	6	0.13	5	Fair	Fair	Medium	Low	Fell	Affected by proposed works	-	-
T900	TS-05	<i>Macaranga tanarius</i>	血桐	*		6	0.21	7	Fair	Fair	Medium	Medium	Transplant	Affected by proposed works	-	unbalanced form, multi-trunked
T901	TS-05	<i>Macaranga tanarius</i>	血桐	*		7	0.16	5	Fair	Fair	Medium	Medium	Transplant	Affected by proposed works	-	-
T902	TS-05	<i>Macaranga tanarius</i>	血桐	*		7	0.17	5	Fair	Fair	Medium	Medium	Transplant	Affected by proposed works	-	forked
T903	TS-05	<i>Ficus microcarpa</i>	細葉榕	*		7	0.13	4	Fair	Fair	High	Medium	Transplant	Affected by proposed works	-	-
T904	TS-05	<i>Ficus microcarpa</i>	細葉榕	*		9	0.19	5	Fair	Fair	High	Medium	Transplant	Affected by proposed works	-	-
T905	TS-05	<i>Bridelia tomentosa</i>	土蜜樹		*	4	0.10	4	Fair	Fair	Low	Low	Retain	-	outside boundary	unbalanced form
T906	TS-05	<i>Ficus microcarpa</i>	細葉榕		*	6	0.13	4	Fair	Fair	High	Medium	Transplant	Conflict with proposed maintenance access	-	-
T907	TS-05	<i>Celtis sinensis</i>	朴		*	6	0.13	4	Fair	Fair	Low	Low	Fell	Affected by proposed works	-	unbalanced form
T908	TS-05	<i>Celtis sinensis</i>	朴		*	6	0.14	4	Fair	Fair	Low	Low	Fell	Affected by proposed works	-	unbalanced form, forked
T909	TS-05	<i>Ficus microcarpa</i>	細葉榕		*	7	0.22	5	Fair	Fair	High	Medium	Transplant	Affected by proposed works	-	-
T910	TS-05	<i>Ficus microcarpa</i>	細葉榕		*	8	0.18	5	Fair	Fair	High	Medium	Transplant	Conflict with proposed maintenance access	-	unbalanced form
T911	TS-05	<i>Ficus microcarpa</i>	細葉榕	*		8	0.25	5	Fair	Fair	High	Medium	Transplant	Affected by proposed works	-	-
T912	TS-05	<i>Celtis sinensis</i>	朴		*	5	0.13	4	Fair	Fair	Low	Medium	Transplant	Affected by proposed works	-	-
T913	TS-05	<i>Melia azedarach</i>	楝	*		8	0.35	7	Fair	Fair	Medium	Medium	Transplant	Affected by proposed works	-	forked
T914	TS-05	<i>Macaranga tanarius</i>	血桐	*		6	0.25	5	Fair	Fair	Medium	Medium	Transplant	Affected by proposed works	-	unbalanced form, multi-trunked
T915	TS-05	<i>Khaya senegalensis</i>	非洲楝	*		9	0.30	5	Fair	Fair	Medium	Medium	Transplant	Conflict with proposed maintenance access	-	unbalanced form
T916	TS-05	<i>Ficus microcarpa</i>	細葉榕	*		5	0.21	4	Fair	Fair	High	Medium	Retain	Not affected by proposed works	-	-
T917	TS-05	<i>Ficus microcarpa</i>	細葉榕	*		7	0.31	5	Fair	Fair	High	Medium	Transplant	Affected by proposed works	-	-
T918	TS-06	<i>Ficus microcarpa</i>	細葉榕	*		2	0.12	0	Fair	Poor	High	Medium	Transplant	Affected by proposed works	-	-
T919	TS-06	<i>Ficus microcarpa</i>	細葉榕		*	3	0.31	2	Fair	Poor	High	Medium	Transplant	Conflict with proposed maintenance access	-	-

Note: The jurisdiction is determined in accordance with Environment, Transport and Works Bureau Technical Circular No.14/2002 for confirmation by relevant departments.



Copyright by Black & Veatch Hong Kong Limited and Government of HKSAR

- LEGEND
- TREE PROPOSED TO BE RETAINED
  - TREE PROPOSED TO BE TRANSPLANTED
  - TREE PROPOSED TO BE FELLED
  - WORK BOUNDARY

SHEET INDEX

[1] [2] [3] [4]
KT2
KT15
KT14
KT13
KT12

Revision	Date	Description	Initial	
Designed	Checked	Drawn	Checked	
Initial	BW	JT	SC	JT
Date	8/05	8/05	8/05	8/05

Contract no. CE 67/98

Contract title  
YUEN LONG, KAM TIN, NGAU TAM MEI & TIN SHUI WAI  
DRAINAGE IMPROVEMENT, STAGE 1  
PHASE 2B - KAM TIN


Drawing title  
TREE SURVEY PLAN  
FOR PROPOSED  
CHANNEL KT15

Drawing no. TS-05	Scale 1:1000 A3 1:500 A1
-------------------	-----------------------------

香港特別行政區政府渠務署  
THE GOVERNMENT OF THE HONG KONG  
SPECIAL ADMINISTRATIVE REGION  
DRAINAGE SERVICES DEPARTMENT

BLACK & VEATCH HONG KONG LIMITED  
博威工程顧問有限公司



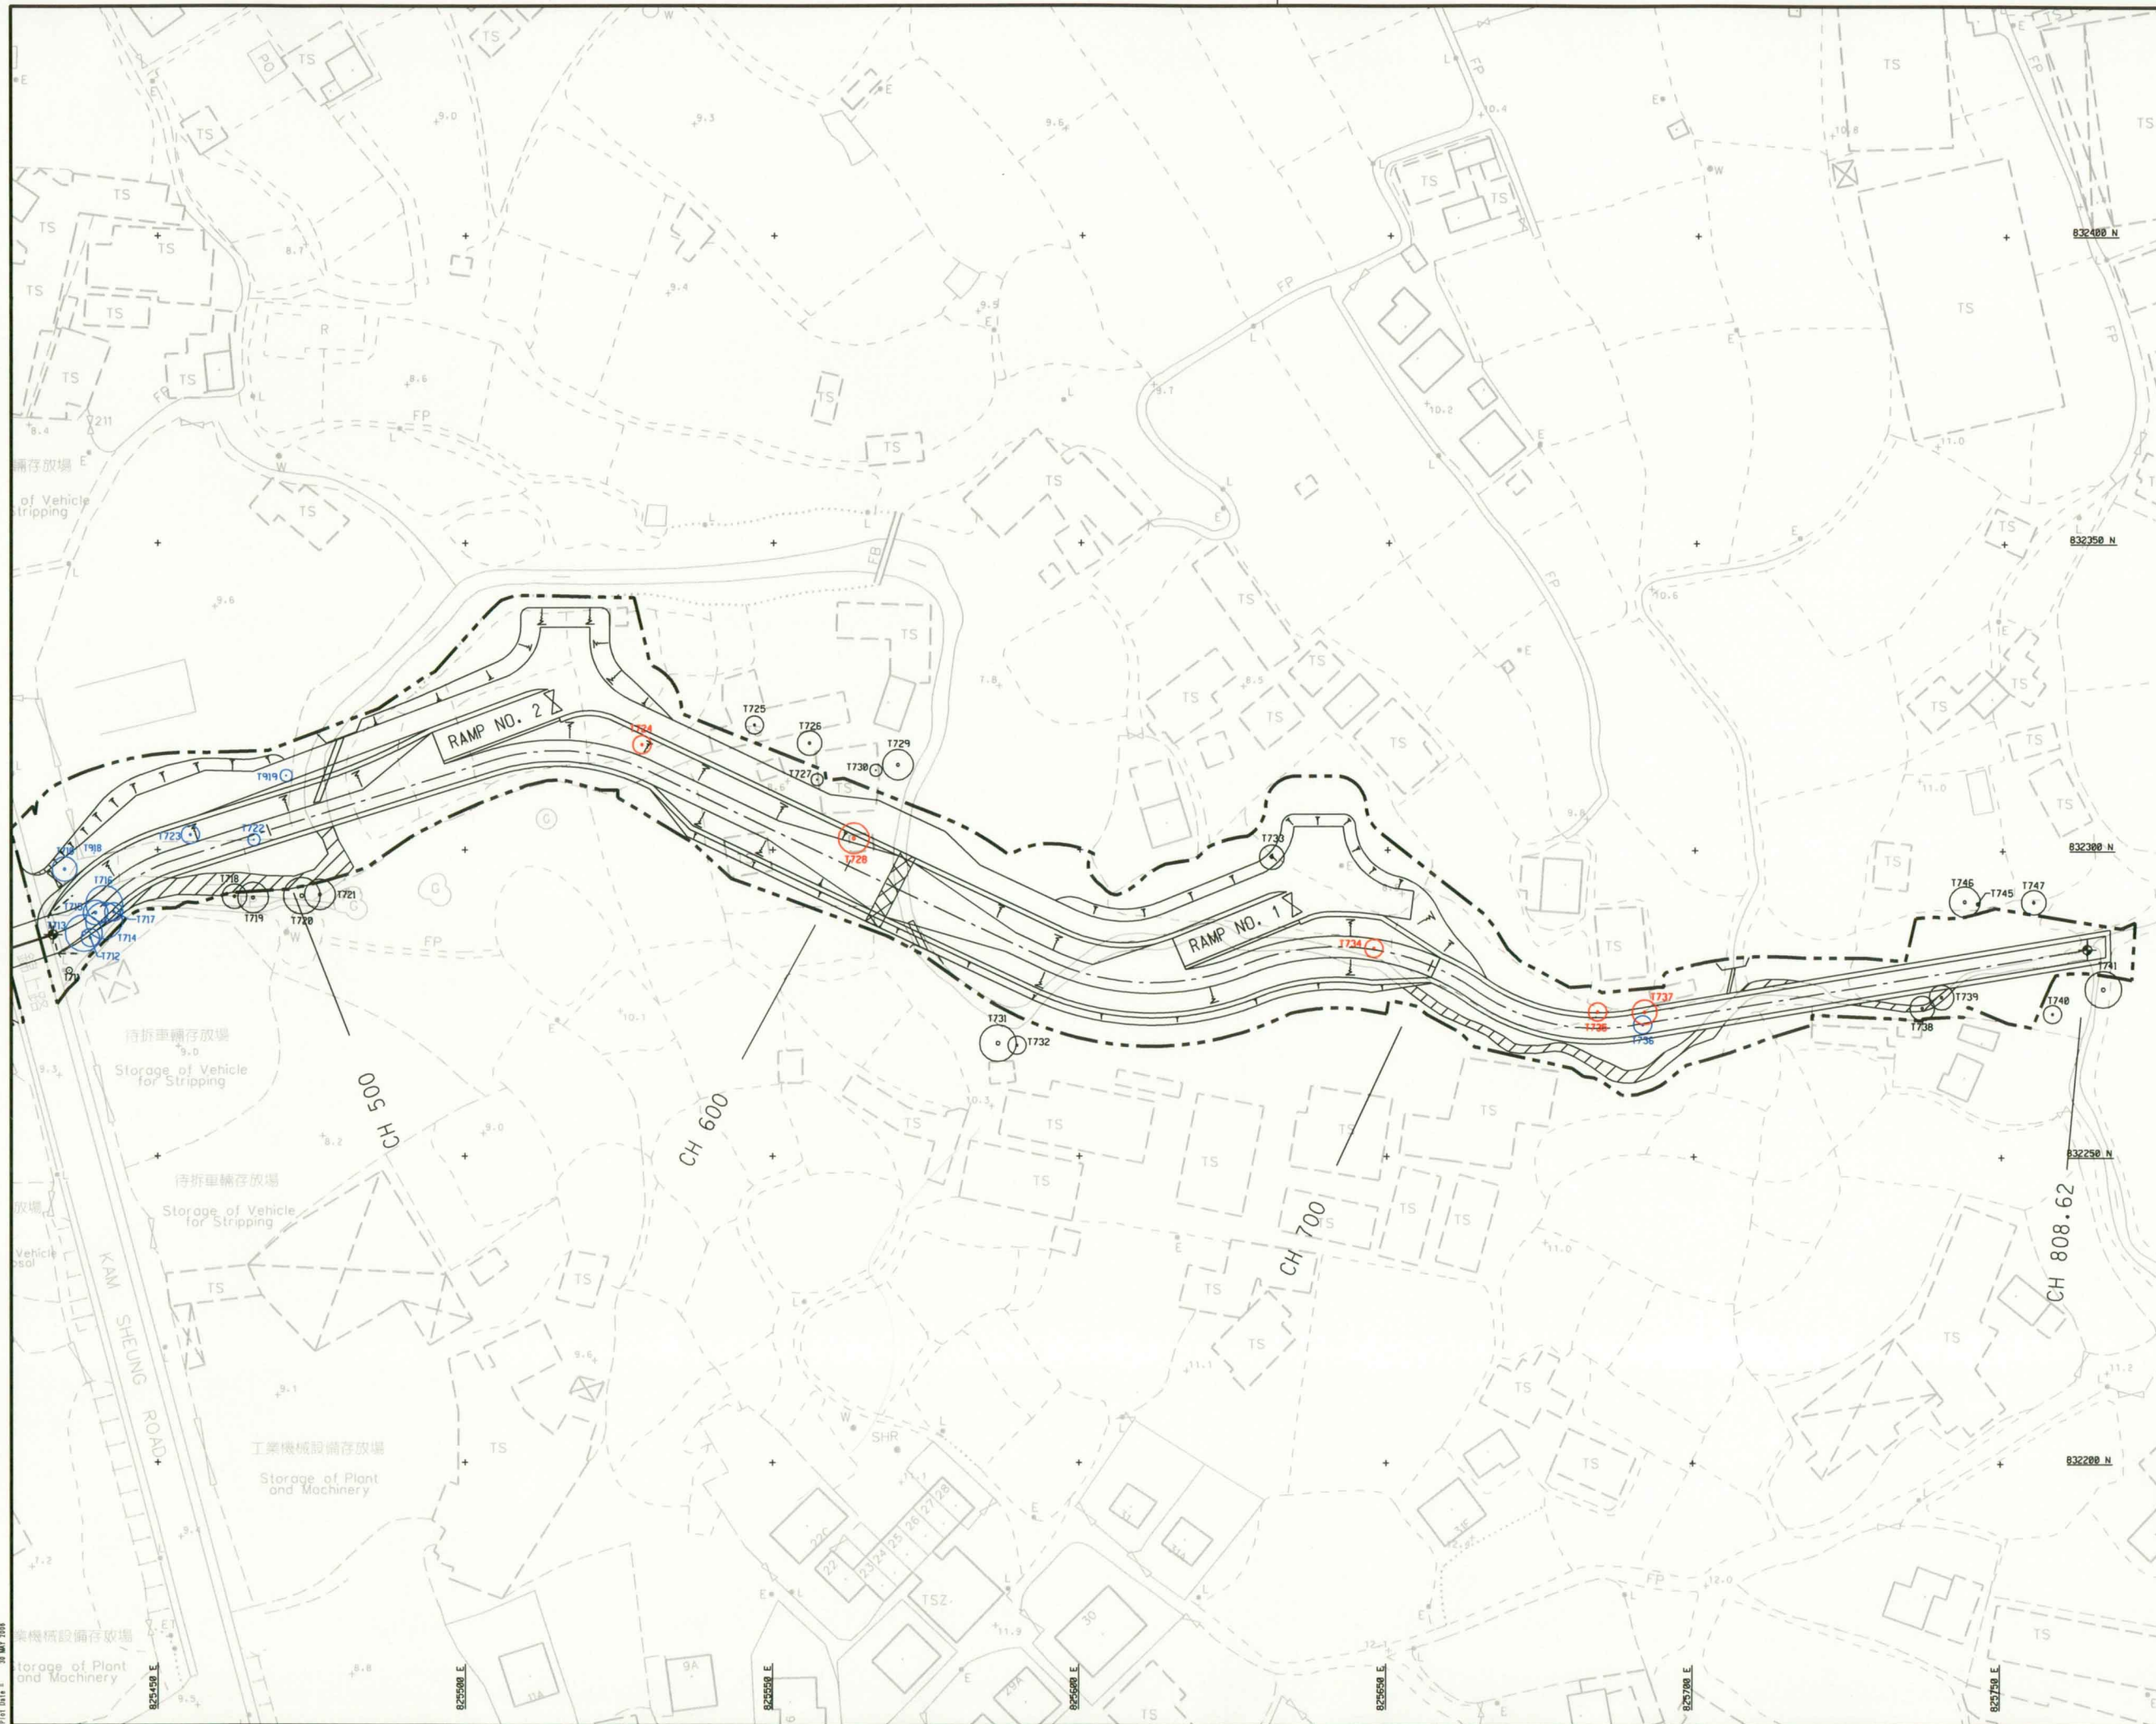

© Copyright by Black & Veatch Hong Kong Limited and Government of HKSAR

- LEGEND
- TREE PROPOSED TO BE RETAINED
  - TREE PROPOSED TO BE TRANSPLANTED
  - TREE PROPOSED TO BE FELLED
  - WORK BOUNDARY

SHEET INDEX

KT2

KT15

KT14

KT13

KT12

Revision	Date	Description		Initial	
		Designed	Checked	Drawn	Checked
Initial	BW	JT	SC	JT	
Date	8/05	8/05	8/05	8/05	8/05

Approved

Contract no. CE 67/98

Contract title  
YUEN LONG, KAM TIN, NGAU TAM MEI & TIN SHUI WAI  
DRAINAGE IMPROVEMENT, STAGE 1  
PHASE 2B - KAM TIN

Drawing title  
TREE SURVEY PLAN  
FOR PROPOSED  
CHANNEL KT15





Drawing no. TS-06	Scale 1:1000 A3 1:500 A1
-------------------	--------------------------------

香港特別行政區政府渠務署  
THE GOVERNMENT OF THE HONG KONG  
SPECIAL ADMINISTRATIVE REGION  
DRAINAGE SERVICES DEPARTMENT

BLACK & VEATCH HONG KONG LIMITED  
博威工程顧問有限公司



© Copyright by Black & Veatch Hong Kong Limited and Government of HKSAR

- LEGEND
-  TREE PROPOSED TO BE RETAINED
  -  TREE PROPOSED TO BE TRANSPLANTED
  -  TREE PROPOSED TO BE FELLED
  -  WORK BOUNDARY

SHEET INDEX

[1] [2] [3] [4]
KT2
KT15
KT14
KT13
KT12

Revision	Date	Description	Initial
Designed	Checked	Drawn	Checked
Initial	BW	JT	SC
Date	8/05	8/05	8/05

Approved

Contract no. CE 67/98

Contract title  
YUEN LONG, KAM TIN, NGAU TAM MEI & TIN SHUI WAI  
DRAINAGE IMPROVEMENT, STAGE 1  
PHASE 2B - KAM TIN

Drawing title  
TREE SURVEY PLAN  
FOR PROPOSED  
CHANNEL KT14

Drawing no.	Scale
TS-07	1:1000 A3 1:500 A1

 香港特別行政區政府渠務署  
THE GOVERNMENT OF THE HONG KONG  
SPECIAL ADMINISTRATIVE REGION  
DRAINAGE SERVICES DEPARTMENT

 BLACK & VEATCH HONG KONG LIMITED  
博威工程顧問有限公司
